642-23-118 Flood Repairs

ID	Task Mode	Name	Duration	Start	Finish
1		**Solicitatin & Award Phase**	**85 days**	**Fri 7/21/23**	**Thu 11/16/23**
2		Package into Force	0 days	Fri 7/21/23	Fri 7/21/23
3		PALT Timeline to Award	30 days	Fri 7/21/23	Thu 8/31/23
4		Award Date	0 days	Thu 8/31/23	Thu 8/31/23
5		Notice to Proceed	10 days	Fri 9/1/23	Thu 9/14/23
6		Materials Submittals & Procurement	45 days	Fri 9/15/23	Thu 11/16/23
7					
8		**First Floor**	**85 days**	**Fri 11/17/23**	**Thu 3/14/24**
9		1st Floor Phase 1 ICRA	5 days	Fri 11/17/23	Thu 11/23/23
10		1st Floor Phase 1	42 days	Fri 11/24/23	Mon 1/22/24
11		1st Floor Phase 2 ICRA	5 days	Tue 1/23/24	Mon 1/29/24
12		1st Floor Phase 2	14 days	Tue 1/30/24	Fri 2/16/24
13		VA Activations PH2 to PH3 First Floor	2 days	Mon 2/19/24	Tue 2/20/24
14		1st Floor Phase 3 ICRA	5 days	Mon 2/19/24	Fri 2/23/24
15		1st Floor Phase 3	14 days	Mon 2/26/24	Thu 3/14/24
16		1st Floor Corridors Weekends	80 days	Fri 11/24/23	Thu 3/14/24
17					
18		**Second Floor**	**239 days**	**Fri 11/17/23**	**Wed 10/16/24**
19		2nd Floor Phase 1 ICRA	5 days	Fri 11/17/23	Thu 11/23/23
20		2nd Floor Phase 1	84 days	Fri 11/24/23	Wed 3/20/24
21		VA Activations PH1 to PH2 Second Floor	14 days	Thu 3/21/24	Tue 4/9/24
22		2nd Floor Phase 2 IICRA	5 days	Thu 3/21/24	Wed 3/27/24
23		2nd Floor Phase 2	84 days	Thu 3/28/24	Tue 7/23/24
24		VA Activations PH2 to PH3 Second Floor	14 days	Wed 7/24/24	Mon 8/12/24
25		2nd Floor Phase 3 ICRA	5 days	Wed 7/24/24	Tue 7/30/24
26		2nd Floor Phase 3	42 days	Wed 7/31/24	Thu 9/26/24
27		VA Activations PH3 Second Floor	14 days	Fri 9/27/24	Wed 10/16/24
28		2nd Floor Corrridor Weekends	150 days	Thu 3/21/24	Wed 10/16/24
29					
30		**Third Floor**	**342 days**	**Fri 11/17/23**	**Mon 3/10/25**
31		3rd Floor Phase 1A ICRA	5 days	Fri 11/17/23	Thu 11/23/23
32		3rd Floor Phase 1A	28 days	Fri 11/24/23	Tue 1/2/24
33		VA Activations PH1A	7 days	Wed 12/27/23	Thu 1/4/24
34		3rd Floor Phase 1 ICRA	5 days	Fri 11/17/23	Thu 11/23/23
35		3rd Floor Phase 1	98 days	Fri 11/24/23	Tue 4/9/24

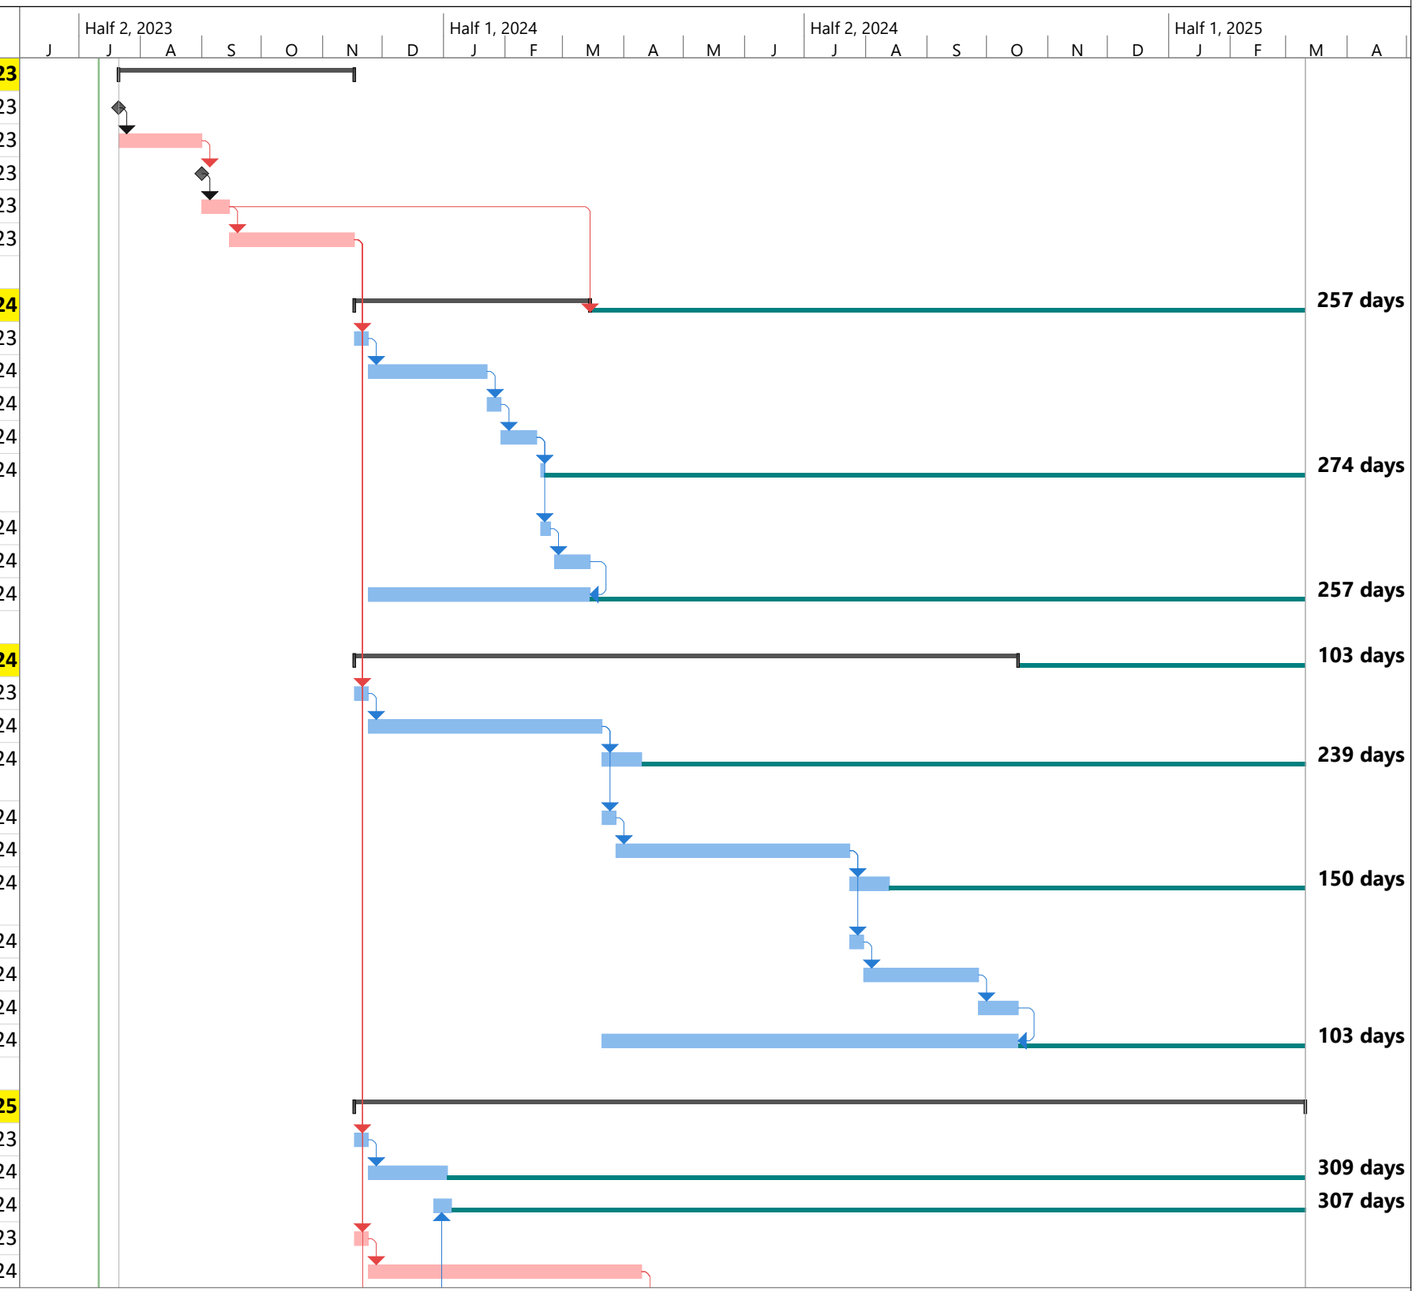

Critical
Critical Split
Task
Split
Milestone
Slack
Slippage
Summary
Project Summary
Rolled Up Critical
Rolled Up Critical Split
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress

642-23-118 Flood Repairs

ID	Task Mode	Name	Duration	Start	Finish
36		VA Activations Phase 1	7 days	Wed 4/10/24	Thu 4/18/24
37		3rd Floor Phase 2 ICRA	5 days	Wed 4/10/24	Tue 4/16/24
38		3rd Floor Phase 2	70 days	Wed 4/17/24	Tue 7/23/24
39		VA Activations PH2 to PH3 Third Floor	14 days	Wed 7/24/24	Mon 8/12/24
40		3rd Floor Phase 3 ICRA	5 days	Wed 7/24/24	Tue 7/30/24
41		3rd Floor Phase 3	84 days	Wed 7/31/24	Mon 11/25/24
42		VA Activtions PH3 to PH4 Third Floor	14 days	Tue 11/26/24	Fri 12/13/24
43		3rd Floor Phase 4 ICRA	5 days	Tue 11/26/24	Mon 12/2/24
44		3rd Floor Phase 4	56 days	Tue 12/3/24	Tue 2/18/25
45		VA Activations PH4 Third Floor	14 days	Wed 2/19/25	Mon 3/10/25
46		3rd Floor Corridors Weekends	240 days	Tue 4/9/24	Mon 3/10/25
47					
48		**Fourth Floor**	**197 days**	**Fri 11/17/23**	**Mon 8/19/24**
49		4th Floor Phase 1A & 1C ICRA	5 days	Fri 11/17/23	Thu 11/23/23
50		4th Floor Phase 1A	21 days	Fri 11/24/23	Fri 12/22/23
51		VA Activations PH1A	7 days	Mon 12/25/23	Tue 1/2/24
52		4th Floor Phase 1C	28 days	Fri 11/17/23	Tue 12/26/23
53		VA Activations PH1C	14 days	Wed 12/27/23	Mon 1/15/24
54		4th Floor Phase 1B ICRA	5 days	Wed 1/3/24	Tue 1/9/24
55		4th Floor Phase 1B	28 days	Fri 3/1/24	Tue 4/9/24
56		VA Activations PH1B	14 days	Wed 4/10/24	Mon 4/29/24
57		4th Floor Phase 1 ICRA	5 days	Fri 11/17/23	Thu 11/23/23
58		4th Floor Phase 1	98 days	Fri 11/24/23	Tue 4/9/24
59		VA Activations Phase 1	14 days	Wed 4/10/24	Mon 4/29/24
60		4th Floor Phase 2 ICRA	5 days	Tue 1/16/24	Mon 1/22/24
61		4th Floor Phase 2	40 days	Tue 1/23/24	Mon 3/18/24
62		VA Activations PH2 to PH3 Fourth Floor	14 days	Tue 3/19/24	Fri 4/5/24
63		4th Floor Phase 3 ICRA	5 days	Tue 3/19/24	Mon 3/25/24
64		4th Floor Phase 3	30 days	Tue 3/26/24	Mon 5/6/24
65		VA Activtions PH3 to PH4 Fourth Floor	14 days	Tue 5/7/24	Fri 5/24/24
66		4th Floor Phase 4 ICRA	5 days	Tue 5/7/24	Mon 5/13/24
67		4th Floor Phase 4	56 days	Tue 5/14/24	Tue 7/30/24
68		VA Activations PH4 Fourth Floor	14 days	Wed 7/31/24	Mon 8/19/24
69		4th Floor Corridors Weekends	195 days	Tue 11/21/23	Mon 8/19/24

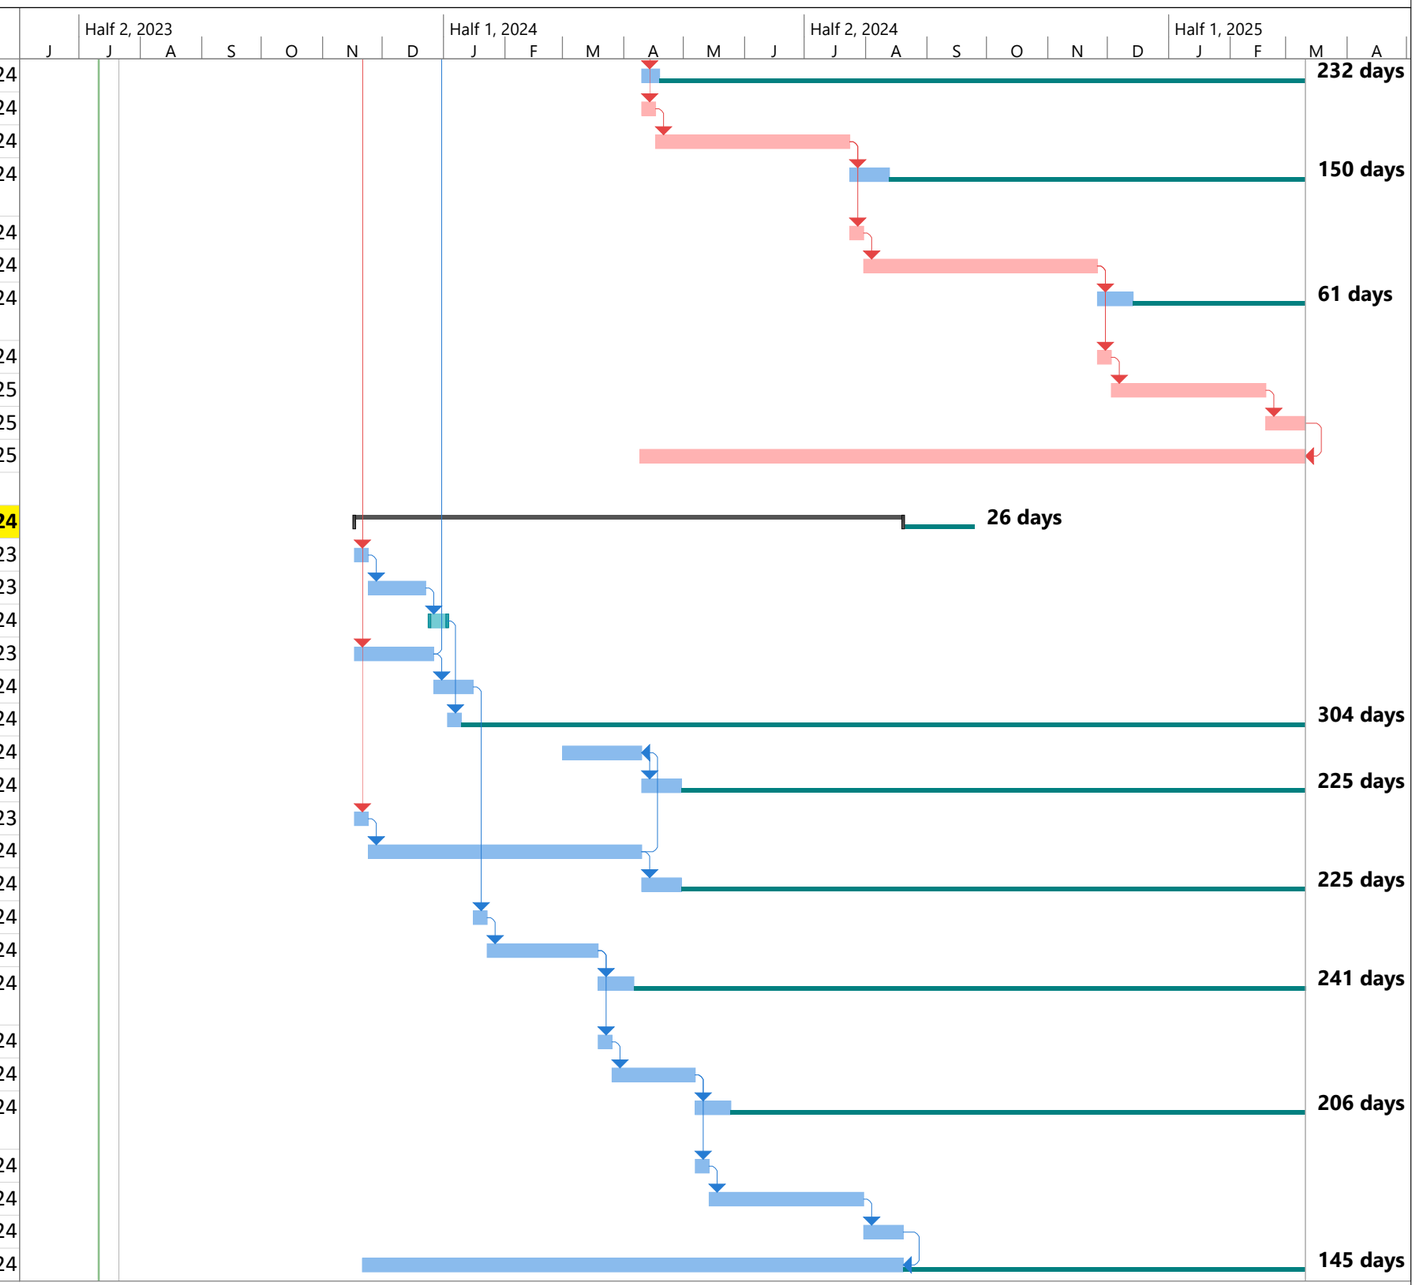

Critical		Slack		Rolled Up Critical Split		Duration-only		External Tasks	
Critical Split		Slippage		Inactive Task		Manual Summary Rollup		External Milestone	
Task		Summary		Inactive Milestone		Manual Summary		Deadline	
Split		Project Summary		Inactive Summary		Start-only		Progress	
Milestone		Rolled Up Critical		Manual Task		Finish-only			
